



ACTUAL DOWN HOLE WELL STATUS

SY-074

RIG: AD - 180

RTKB: 513.6ft

TVD: 4,353.8ft

Ground Level: 488.6ft

TD: 7,791.0ft

509.7ft

WELLHEAD DETAILS

Discreption	MAKER	SIZE(in)	Working Pressure (psi)
X-Mass Tree	GE	11.000	5,000.00
Double Stud. Adapter	GE	11.000	5,000.00
Tubing Hanger	GE	10.000	5,000.00
Tubing Head Spool	GE	11.000	5,000.00
Casing Hanger	WG	13.625	3,000.00
Casing Head Housing	WG	13.375	3,000.00

CONDUCTOR

Item description	OD(in)	ID(in)	Length(ft)	MD base(ft)
Casing, Casing, in, ppf, , , 18.625			180.00	209.0
Casing Shoe, Casing Shoe, in, ppf, , , 18.625			2.00	211.0

SURFACE CASING

Item description	OD(in)	ID(in)	Length(ft)	MD base(ft)
Casing, Casing, in, ppf, , , 13.375			21.60	50.6
Casing, Casing, in, ppf, , , 13.375			123.60	174.2
Casing, Pup Joint, in, ppf, , , 13.375			19.72	193.9
Casing, Casing, in, ppf, , , 13.375			956.51	1,150.4
Casing, Casing Float Collar, in, ppf, , , 13.375			1.89	1,152.3
Casing, Casing, in, ppf, , , 13.375			82.88	1,235.2
Casing, Casing Float Shoe, in, ppf, , , 13.375			1.82	1,237.0

INTERMEDIATE CASING

Item description	OD(in)	ID(in)	Length(ft)	MD base(ft)
Casing, Casing, in, 47.00 ppf, , , 9.625		8.755	4,387.00	4,416.0
Float Collar, Float Collar, in, ppf, , , 9.625		8.755	1.60	4,417.6
Casing, Casing, in, 47.00 ppf, , , 9.625		8.755	86.95	4,504.6
Casing Shoe, Casing Shoe, in, ppf, , , 9.625		8.755	1.85	4,506.4

PRODUCTION LINER

Item description	OD(in)	ID(in)	Length(ft)	MD base(ft)
Xpress Liner Hanger WFD	7.000	6.184	25.09	2,736.8
Casing, 7 in, 29 ppf, L-80, VAM® TOP,	7.000	6.184	1,890.40	4,627.2
Landing collar	7.000	6.184	1.71	4,628.9
Casing, 7 in, 29 ppf, L-80, VAM® TOP,	7.000	6.184	40.46	4,669.4
Float collar	7.000	6.184	2.28	4,671.6
Casing, 7 in, 29 ppf, L-80, VAM® TOP	7.000	6.184	128.35	4,800.0
Casing Shoe	7.000	6.184	2.46	4,802.5

SINGLE TUBING STRING


#	Item description	OD(in)	Body ID(in)	Length(ft)	MD base(ft)
1	GE HGR, TBG, SGLE 10" x 4 1/2 IN VAM TOP THD BTM & 10000	10.000	3.900	2.15	25.0
2	4-1/2" PJ 12.6 LB/FT L-80	4.920	3.958	4.13	29.1
3	4-1/2" V-TOPTUBING 12.6# LB/FT L-80 +2x10' Pup Joints	4.920	3.958	152.48	181.6
4	4-1/2" PUP JOINT 12.6 LB/FT L-80	4.921	3.958	9.03	190.6
5	4-1/2" FLOW COUPLING L-80	4.920	3.958	5.73	196.3
6	4-1/2 TRMAXX-8E-MTM, 3.813 R, 7.220 OD, 8K,	7.460	5.600	5.06	201.4
7	4-1/2" FLOW COUPLING L-80	4.397	2.992	5.57	207.0
8	4-1/2"-3-1/2" XO P.JOINT 12.6 LB/FT L-80	3.920	2.992	3.35	210.3
9	3-1/2" P.JOINT 9.2 LB/FT L-80	3.920	2.992	4.76	215.1
10	3-1/2" V-TOP TUBING 9.2 LB/FT L-80 + 1x3' PUP JOINT	3.920	2.992	3,872.67	4,087.7
11	3-1/2" PUP JOINT 9.2 LB/FT L-80	3.920	2.992	9.95	4,097.7
12	PRAXIS ISOPAX PRO PACKER 7" 23-29 lb/ft CSG,	6.020	2.990	6.42	4,104.1
13	3-1/2" PUP JOINT 9.2 LB/FT L-80	3.920	2.992	9.93	4,114.0
14	3-1/2" V-TOP TUBING 9.2 LB/FT L-80 1 JNT	3.920	2.867	30.57	4,144.6
15	3-1/2" HANDLING SUB 9.2 LB/FT L-80 VTOP	3.500	2.867	6.10	4,150.7
16	3-1/2" BAKER F NIPPLE 2.813" @ 51 DEG	3.910	2.813	1.65	4,152.4
17	Y-TOOL + RMS SYSTEM COMPLETE FOR 7" CASING 29#	5.624	2.867	3.00	4,155.4
18	TELESWIVEL ASSY. UBT PIN DOWN CONNECTION	2.750	5.513	4.00	4,159.4
19	Bypass Tubing 2-7/8" PTX Box x Pin (5x15+1x6.8)	5.825	1.901	85.24	4,244.6
20	Pump Support Block Body w/15ft x 2 joints (2 3/8 V-TOP Pin)	2.375	1.901	30.00	4,274.6
21	Crossover 2-3/8" UBT Box X 3-1/2" V.T Pin	3.500	1.901	2.30	4,276.9
22	Crossover 3-1/2" V.T B x 2-7/8" TSH 3SB P	3.500	2.321	9.95	4,286.8
23	2-7/8" TSH Tubing 6.5 LB/FT L-80 2 JTS	2.875	2.441	61.21	4,348.0
24	2 7/8" Pup joint 6.5# THS 3SB Box x Pin	3.920	2.441	10.25	4,358.3
25	3-1/2" 9.2 LB/FT L-80 + 2-7/8" x 3-1/2" XO 9.2 LB/FT L-80	3.970	2.992	5.22	4,363.5

ESP STRING

#	Item description	OD(in)	Body ID(in)	Length(ft)	MD base(ft)
1	Y-TOOL ZENITH SYSTEM COMPLETE FOR 7" CASING 29#	5.624	2.750	3.00	4,161.5
2	PUMP SUB 1.900" ZFC Pin x 1.900" ZFC Pin	1.900	1.300	9.58	4,171.0
3	Crossover: 1.900" ZFC Box x 2-3/8" EUE Pin	2.375	0.000	0.60	4,171.6
4	DISCHARGE PRESSURE SUB:2-3/8"-8RD EUE BOX/PIN 1/8"	1.900	0.000	0.62	4,172.3
5	BOH 2-3/8"-8RD EUE-319SER CR3 PN 2013070061	3.190	0.000	0.66	4,172.9
6	2xPUMP, NB(1100-1800)H CMP AR1:1 CR2C S14 70STG	3.190	0.000	22.00	4,194.9
7	MULTIPHASE PUMP, N319MPP1500 CMP AR2 CR2S S14	3.580	0.000	7.80	4,202.7
8	INTAKE, N319I 319H/319B CR3 0.67" S14 PN 3003070014	3.190	0.000	0.78	4,203.5
9	PROTECTOR, N319TMP BPB- 319H/ CR2S HT HL S11	3.190	0.000	5.65	4,209.1
10	PROTECTOR, N319TMP -SBPB /319B CR2S HT HL S11	3.190	0.000	5.65	4,214.8
11	MOTOR, N319PM84 15800V 6.0RPM UT CR2C HT NDS2	3.190	0.000	35.30	4,250.1
12	DOWNHOLE SENSOR, NDS2 319 DES2 5800PSI CR2C MOD	0.000	0.000	2.95	4,253.0
13	CROSSOVER 2-3/8" EUE Box x 2-3/8" NU Pin	2.938	0.000	0.61	4,253.7
14	SPEAR CROSSOVER 2-3/8" 4.7# EUE Pin x 2-3/8" NU Box	0.000	0.000	0.42	4,254.1
15	Spear (ABOVE Saddle) + bullnose	0.000	0.000	9.00	4,263.1

PRODUCTION LINER

#	Item description	OD(in)	Body ID(in)	Length(ft)	MD base(ft)
1	5-1/4" 20 FT TBR (TOP OF LINER) @ 55deg	5.847	5.260	22.00	4,363.6
2	SLB TOP PACKER, 7" X 4-1/2"	5.916	4.190	3.76	4,367.4
3	COUPLING,5.00/18,VTOP B X B, L80	5.626	4.400	0.86	4,368.2
4	5" HPS LINER HANGER,5.00/18 X 07.00/29-32,VTOP P X P	5.180	4.190	6.46	4,374.7
5	X-over 5" #18 Vam Top Box x 4 1/2" #13.5 Vam Top Pin	5.630	3.880	1.73	4,376.4
6	4-1/2" PUP JOINT Vam Top L-80 12.6 LB/FT	4.950	3.960	9.13	4,385.5
7	14 VAM TOP TUBING 4.5" 12.6 LB/FT L80 + PJ's	4.950	3.960	443.26	4,828.8
8	4-1/2" OIL SWELL PACKER#6 (4824.87 ft TO 4829.87 ft)	5.540	3.960	5.00	4,833.8
9	5 VAM TOP TUBING 4.5"12.6 LB/FT L80 + PJ's	4.950	3.960	188.62	5,022.4
10	4-1/2" SLB ICD# 8 13.5# L80 VAM TOP 4mm x 4 nozzles Open	4.950	3.890	5.67	5,028.1
11	7 VAM TOP TUBING 4.5"12.6 LB/FT L80 + PJ's	4.950	3.960	223.48	5,251.6
12	4-1/2" SLB ICD# 7 13.5# L80 VAM TOP 4mm x 4 nozzles Open	4.950	3.890	5.67	5,257.2
13	4 VAM TOP TUBING 4.5"12.6 LB/FT L80 + PJ's	4.950	3.960	142.89	5,400.1
14	4-1/2" OIL SWELL PACKER#5 (5396.19 ft TO 5401.19 ft)	5.540	3.960	5.00	5,405.1
15	4 VAM TOP TUBING 4.5"12.6 LB/FT L80 + PJ's	4.950	3.960	157.52	5,562.7
16	4-1/2" SLB ICD# 6 13.5# L80 VAM TOP 4mm x 4 nozzles Open	4.950	3.890	5.67	5,568.3
17	8 VAM TOP TUBING 4.5"12.6 LB/FT L80 + PJ's	4.950	3.960	253.45	5,821.8
18	4-1/2" SLB ICD# 5 13.5# L80 VAM TOP 4mm x 4 nozzles Open	4.950	3.890	5.67	5,827.4
19	5 VAM TOP TUBING 4.5"12.6 LB/FT L80 + PJ's	4.950	3.960	174.73	6,002.2
20	4-1/2" OIL SWELL PACKER#4 (5998.24 ft TO 6003.24 ft)	5.540	3.960	5.00	6,007.2
21	1 VAM TOP TUBING 4.5"12.6 LB/FT L80 + PJ's	4.950	3.960	67.45	6,074.6
22	4-1/2" SLB AICD#4 13.5# L80 VAM TOP 2.5mm x 2 LV nozzles Open	4.950	3.890	2.84	6,077.5
23	6 VAM TOP TUBING 4.5"12.6 LB/FT L80 + PJ's	4.950	3.960	192.57	6,270.0
24	4-1/2" SLB AICD#3 13.5# L80 VAM TOP 2.5mm x 2 LV nozzles Open	4.950	3.890	2.84	6,272.9
25	4 VAM TOP TUBING 4.5"12.6 LB/FT L80 + PJ's	4.950	3.960	143.76	6,416.6
26	4-1/2" OIL SWELL PACKER#3 (6412.70 ft TO 6417.70 ft)	5.540	3.960	5.00	6,421.6
27	2 VAM TOP TUBING 4.5"12.6 LB/FT L80 + PJ's	4.950	3.960	97.50	6,519.1
28	4-1/2" SLB AICD#2 13.5# L80 VAM TOP 2.5mm x 2 LV nozzles Open	4.950	3.890	2.84	6,522.0
29	6 VAM TOP TUBING 4.5" 12.6 LB/FT L80 + PJ's	4.950	3.960	192.68	6,714.7
30	4-1/2" SLB AICD #1 13.5# L80 VAM TOP 2.5mm x 2 LV nozzles Open	4.950	3.890	2.84	6,717.5
31	4 VAM TOP TUBING 4.5"12.6 LB/FT L80 + PJ's	4.950	3.960	143.50	6,861.0
32	4-1/2" OIL SWELL PACKER#2 (6857.06 ft TO 6862.06 ft)	5.540	3.960	5.00	6,866.0
33	3 VAM TOP TUBING 4.5" 12.6 LB/FT L80 + PJ's	4.950	3.960	126.90	6,992.9
34	4-1/2" SLB ICD# 4 13.5# L80 VAM TOP 4mm x 4 nozzles Open	4.950	3.890	5.67	6,998.6
35	7 VAM TOP TUBING 4.5"12.6 LB/FT L80 + PJ's	4.950	3.960	222.37	7,220.9
36	4-1/2" SLB ICD# 3 13.5# L80 VAM TOP 4mm x 4 nozzles Open	4.950	3.890	5.67	7,226.6
37	4 VAM TOP TUBING 4.5" 12.6 LB/FT L80 + PJ's	4.950	3.960	142.33	7,368.9
38	4-1/2" OIL SWELL PACKER#1 (7365 ft TO 7370 ft)	5.540	3.960	5.00	7,373.9
39	1 VAM TOP TUBING 4.5" 12.6 LB/FT L80 + PJ's	4.950	3.960	66.00	7,439.9
40	4-1/2" SLB ICD# 2 13.5# L80 VAM TOP 4mm x 4 nozzles Open	4.950	3.890	5.67	7,445.6
41	6 VAM TOP TUBING 4.5"12.6 LB/FT L80 + PJ's	4.950	3.960	192.73	7,638.3
42	4-1/2" SLB ICD# 1 13.5# L80 VAM TOP 4mm x 4 nozzles Open	4.950	3.890	5.67	7,644.0
43	4 VAM TOP TUBING 4.5" 12.6 LB/FT L80 + PJ's	4.950	3.960	127.15	7,771.2
44	4-1/2" RAS L-80 VTOP w/4-1/2" BLANK 12.6 LB/FT L80 VT	5.750	3.960	17.61	7,788.8
45	4-1/2" #12.6 Vam Top SLB Eccentric shoe (TSH Blue B)	4.950	3.960	3.17	7,791.9

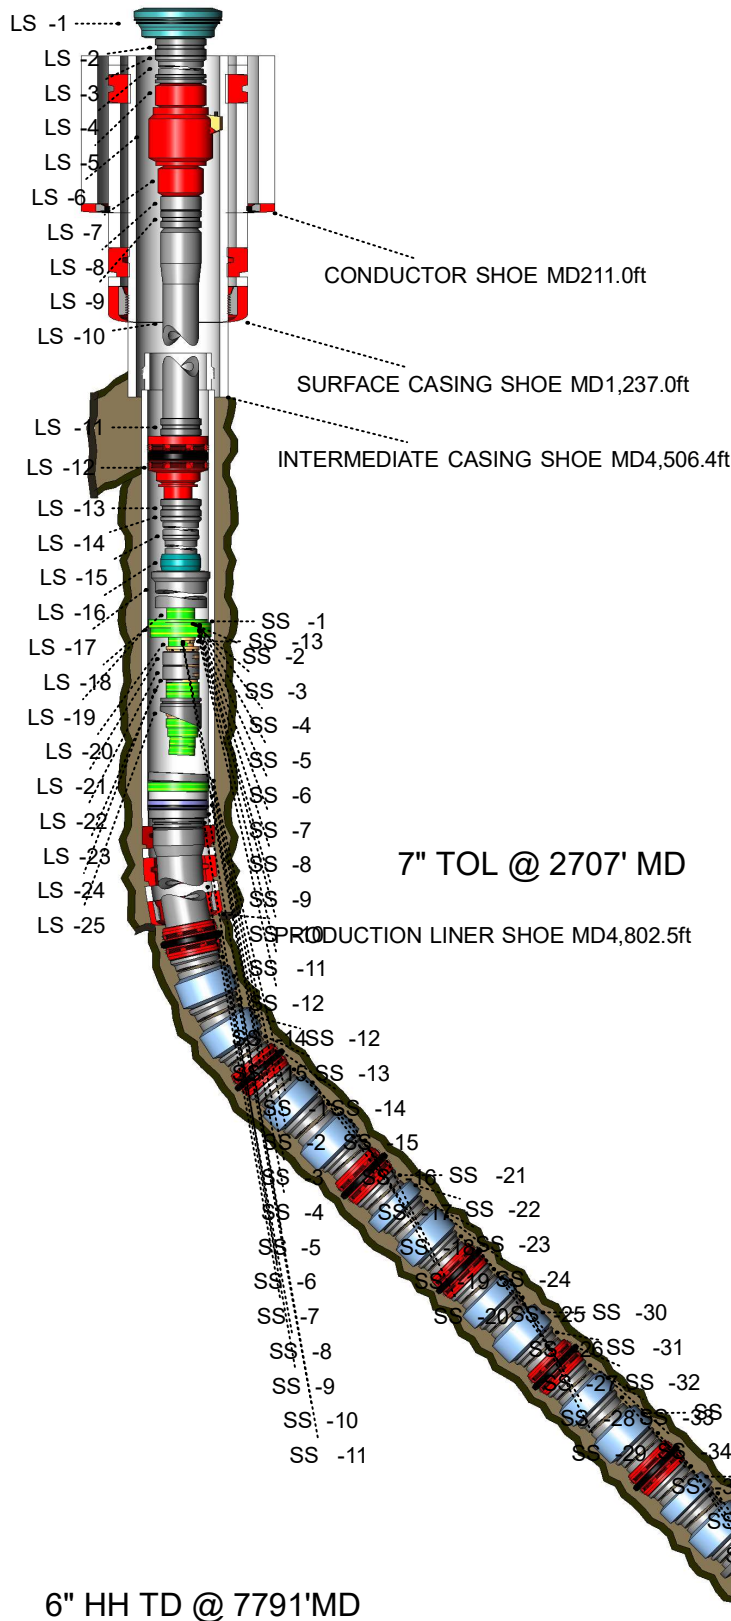

REVISION :	FINAL	DATE :	11-Aug-24	COMPLETION ENGINEER :	Hisham Alshaghnoobi	DRILLING SUPERVISOR :	Rojan Bacina
------------	-------	--------	-----------	-----------------------	---------------------	-----------------------	--------------
